



Flow Test Summary




Prior to conducting test you must contact Inspection Services at 480-312-5750 to activate permit and schedule test date and inspection.

Project Address: 10855 N. 116th St, Scottsdale, AZ 85259
Encroachment Permit No. C68749 Date of Test: 5/19/22 Time of Test: 7:00 am

Test requires using two (2) hydrants on the water system.

1. Attach water quarter section map identifying (#1) pressure and (#2) flow hydrant used to conduct the test OR
2. Show location of pressure hydrant and flow hydrant with cross streets and distance between hydrants and main size tested below.

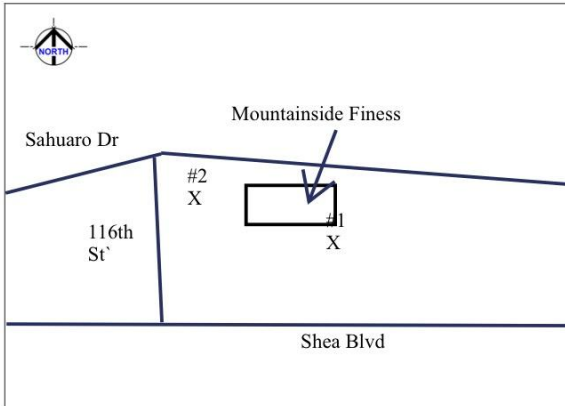

Test Data

Static pressure: 90 psi
 Residual pressure: 60 psi
 Pitot reading: 50 psi
 Flow GPM: 1190 gpm

Hydrant orifice Diameter: 2.5"
 Coefficient of Discharge: 0.9

Contractor:
Halo Fire Protection

Signature(s) of contractor's employees conducting test:

Carl Roth

Area Inspector present at test:

Vince Cusumano

Planning & Development Services Department

7447 E Indian School Road, Suite 105, Scottsdale, AZ 85251 • Phone: 480-312-7000 • Fax: 480-312-7088

21-DR-2022

8/26/2022
